

elite precast

TF7 4QW
01952 728852


Report Title	b11 flat
Report Date	28 Jun 2022 15:14
Compiled By	steven James Savigar

Signature 

Customer Company Name	elite precast concrete
-----------------------	------------------------

Test Title


10:51 AM 16 Feb 2022

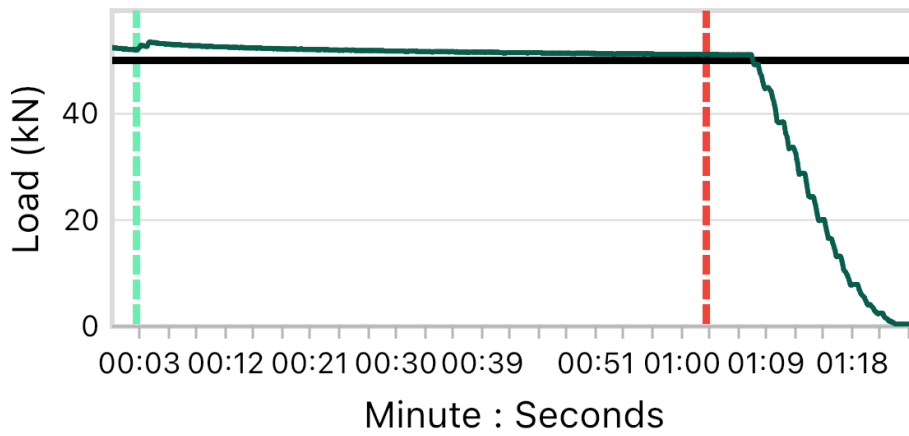

Date & Time	16 Feb 2022 10:51	Maximum Load Achieved	53.5 kN
Target Load	50.0 kN	Device SN	228
Timed Section Started	00:02	Timed Section Finished	01:02
Timed Section Length	01:00	Next Calibration Date	02 Dec 2022
Test Result	Test Result Pass		

Notes


fresh out of mould this morning pin passed and concrete

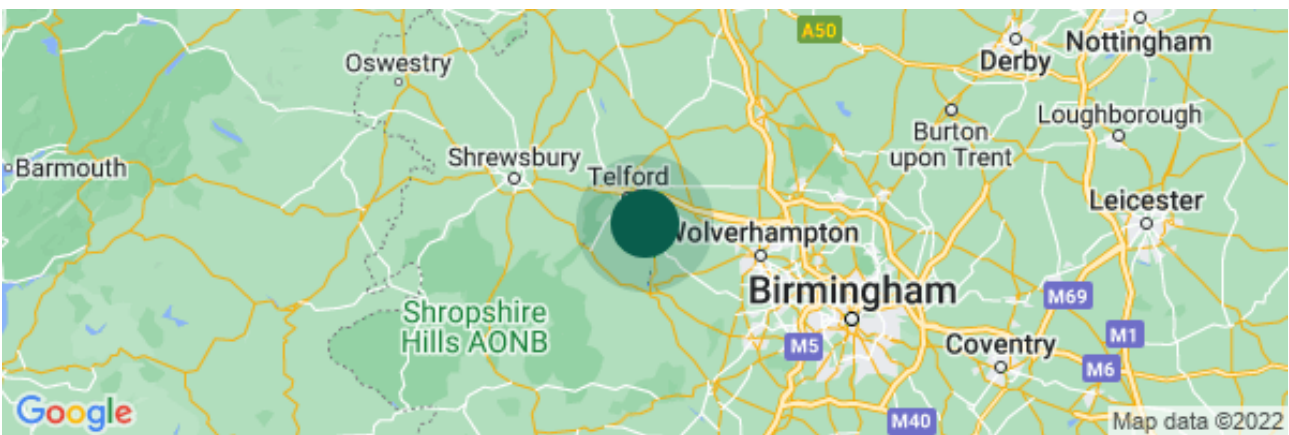




Test Title

04:06 PM 26 Apr 2022

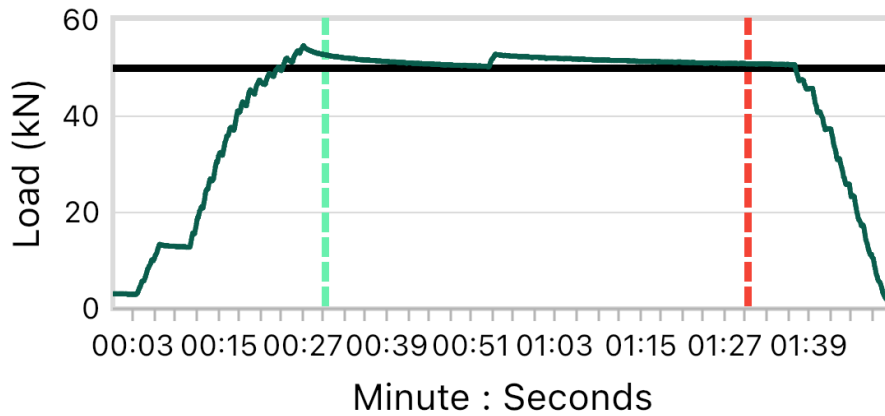

Date & Time	26 Apr 2022 17:06	Maximum Load Achieved	54.7 kN
Target Load	50.0 kN	Device SN	228
Timed Section Started	00:30	Timed Section Finished	01:30
Timed Section Length	01:00	Next Calibration Date	02 Dec 2022
Test Result	Test Result Pass		


Notes

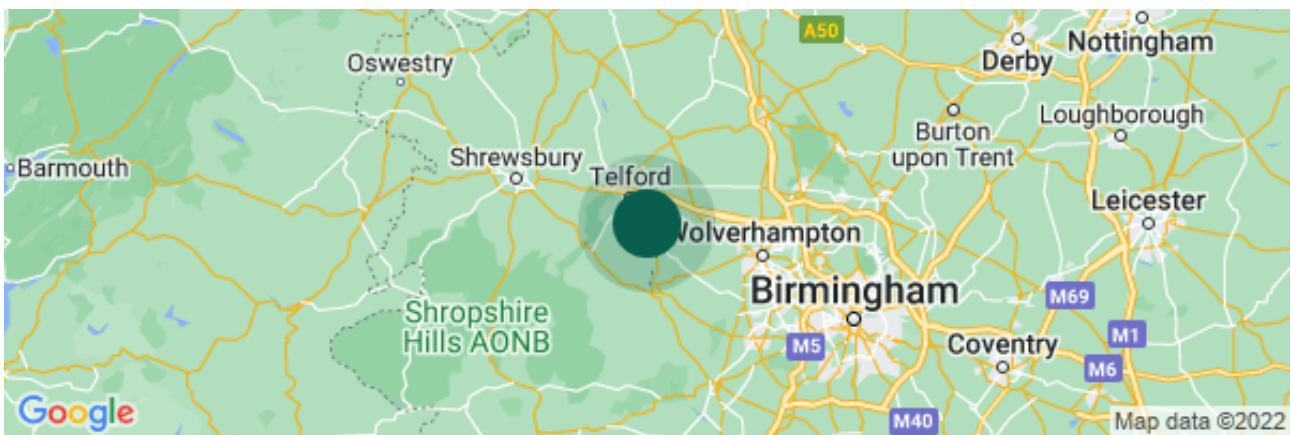




Test Title

04:01 PM 26 Apr 2022

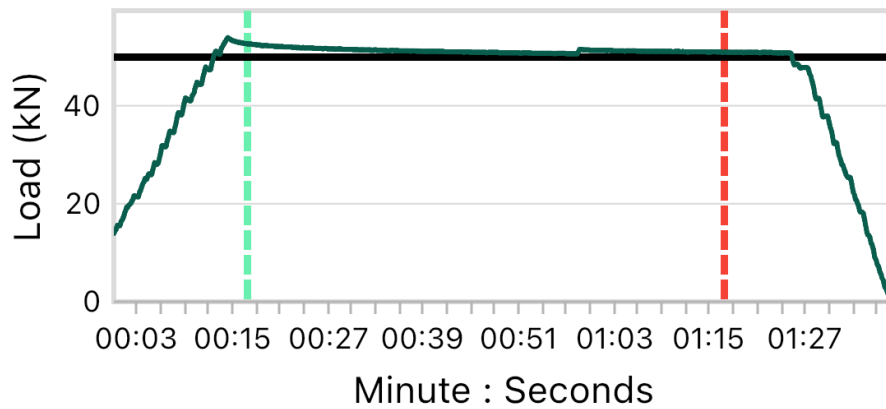

Date & Time	26 Apr 2022 17:01	Maximum Load Achieved	53.9 kN
Target Load	50.0 kN	Device SN	228
Timed Section Started	00:16	Timed Section Finished	01:16
Timed Section Length	01:00	Next Calibration Date	02 Dec 2022
Test Result	Test Result Pass		


Notes

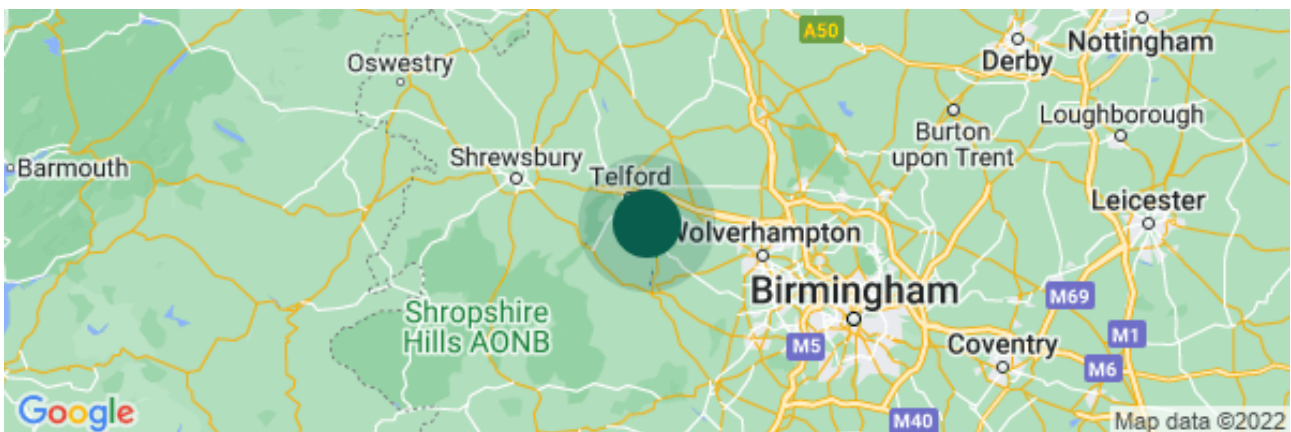



Test Title

04:06 PM 26 Apr 2022

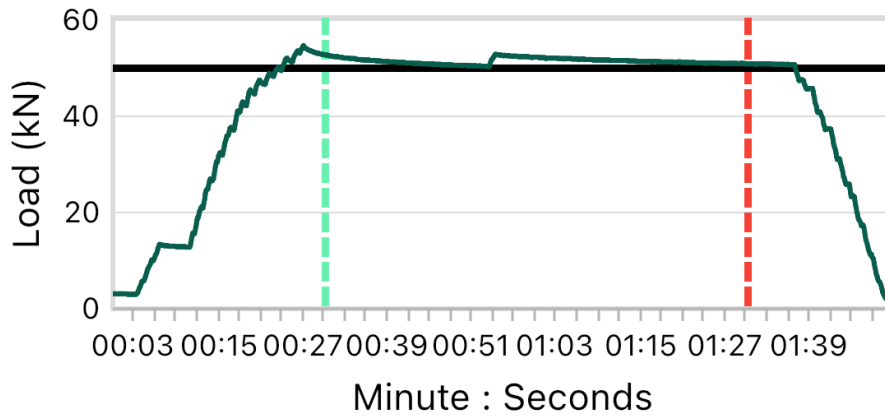

Date & Time	26 Apr 2022 17:06	Maximum Load Achieved	54.7 kN
Target Load	50.0 kN	Device SN	228
Timed Section Started	00:30	Timed Section Finished	01:30
Timed Section Length	01:00	Next Calibration Date	02 Dec 2022
Test Result	Test Result Pass		

Notes

