




SITE LAYOUT

1:200

TOTAL BLOCK SCHEDULE - ALL BAYS				
Type Mark	Type	Count	Volume	Weight (t)
LG4-800	LG4 800x800x800	35	17.92 m <sup>3</sup>	43.008
LG6-1200	LG6 1200x800x800	16	12.29 m <sup>3</sup>	29.4912
LG8-1600	LG8 1600x800x800	949	971.78 m <sup>3</sup>	2332.2624
LG-BENDI	LG BENDI BLOCK	5	5.12 m <sup>3</sup>	12.288
LG-SPREADER	LG Spreader	127	130.05 m <sup>3</sup>	312.1152
Grand total: 1132			1132	1137.15 m <sup>3</sup> 2729.1648


NOTES

- Contractor to check all dimensions and levels and report any errors or omissions to the engineer. All design, materials, construction and workmanship to be in accordance with the requirements of the appropriate British Standards / European Codes, or Codes of Practice unless varied by the specification drawings.
- This drawing to be read in conjunction with all relevant Architects, Engineers and Specialists drawings together with the specification.
- All dimensions and levels not shown, to be taken from relevant Architects details.
- All indicated dimensions between or to existing elements to be checked on site before fabrication.
- Drawing is not to be scaled physically or electronically, if in doubt ask.
- All dimensions in millimetres except levels which are in metres.

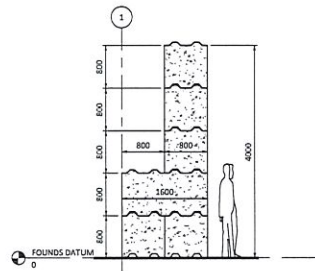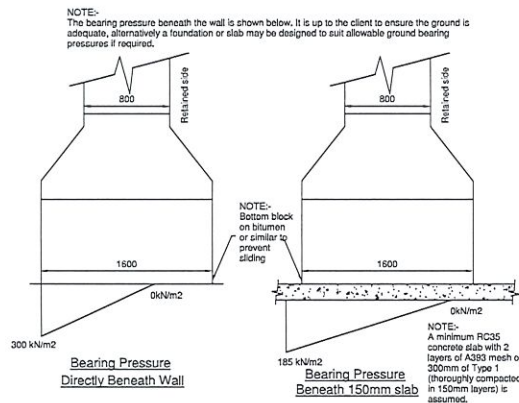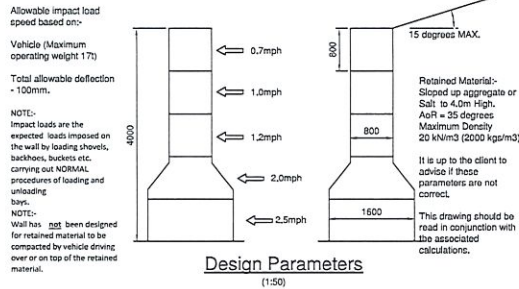

TYPICAL SECTION 01 - PERIMETER WALLS

1:50

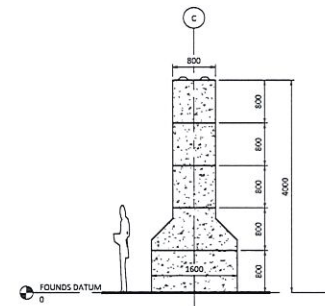

TYPICAL SECTION 02 - DIVIDING WALLS

1:50

Rev	Description	Date	By	CHK
-----	-------------	------	----	-----

**CLP Structures**  
STRUCTURAL ENGINEERING CONSULTANTS

8 The Grove, Halesowen, Bristol, BS39 6ES  
Tel: 0117 3706357 Email: mail@clp-structures.co.uk  
Registered UK Company No. 8929503

**ELITE**  
PRECAST CONCRETE

Halesfield 9, Telford, Shropshire TF7 4QWS  
Tel: 01952 588885 Fax: 01952 582011  
Email: sales@eliteprecast.co.uk

Project: MICHELDEVER DEPOT - OPTION A

Title: SITE PLAN & DESIGN CONDITIONS

PROJECT STATUS INFORMATION			
Original Scale (NAS)	Drawn	Checked	Rev
As Indicated	Author	Checker	
Project Number	Date	Drawing Number	
CLP096	20.01.16	1-001	
