
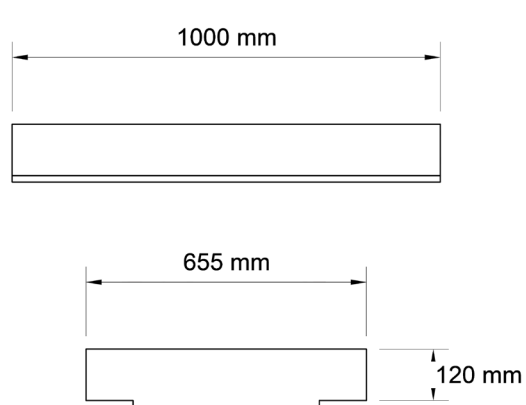


Load Test Result 1197 Lid

Vertical Load Test Report

Factory Production Control Manual	Version No.: 001	PR/PR/REV001/RJM/07.09.2020
1197 Duct Lid		Form QS9 Rev002/RJM/EPC/June16
Dimensional Checks  <p>Tolerances : Thickness not less than normal $\pm 5.0\text{mm}$</p>	Date Made: 19/08/2020 Date Tested: 07/09/2020 Test Age: 19 Bedding Condition: OK Age of the Bed: 3 Days Proof load applied (Fp): 400 KN Residual crack width (max. 0.15mm): N/A Collapse Load (Fu) (cover and ITT only) (min 300kN) 400 KN: No Failure Visual appearance (cracks or surface voids): 0 Acceptable	
Vertical Load Test Arrangement 		
Tested By : S.Savigar		Result (PASS/FAIL): PASS

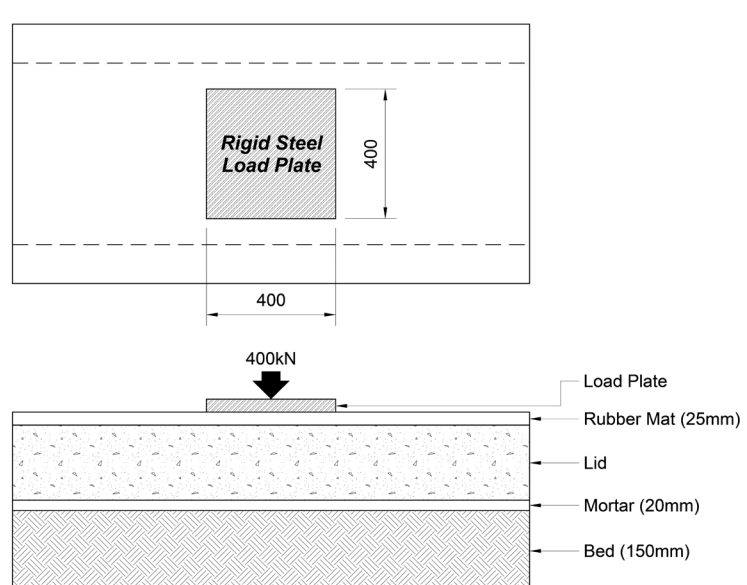

Elite Precast Concrete Limited
Halesfield 9, Telford, Shropshire TF7 4QW
Tel: 01952 588885
www.eliteprecast.co.uk
